

FIELD INSPECTION

Project Name:	Mountain Valley Pipeline	Inspector:	Matthew Grant
Inspection Date:	Tuesday, January 14, 2020	Project Contact:	Brian Clauto
Spread: Montgomery County MP 229-231 AR-MN 270.01 ATWS 701	Spread H	Weather (Wet/Dry/Rain):	Wet

STAGE OF CONSTRUCTION: (Check all that apply)

- Clearing Rough Grading Trench Excavation Pipe Assembly, Testing & Installation
 Backfilling and Grade Restoration Final Grading & Stabilization Other: Dormant

- | | | Yes | No | N/A |
|---|---|-------------------------------------|-------------------------------------|--------------------------|
| 1 | Are controls installed and implemented in accordance with the approved erosion and sediment control plan and stormwater management plans? | <input checked="" type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> |
| 2 | Are all control measures properly maintained in effective operating condition in accordance with good engineering practices and, where applicable, manufacturer specifications? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | <input type="checkbox"/> |
| 3 | Areas of offsite sediment deposition were observed? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | <input type="checkbox"/> |

Comments:

- Inspected designated streams and wetlands included S-MM 11, S-F15, S-16A & B, S-C33, S-C36, S-MM31, S-C25, S-C24, S-C21, S-OO11.
- ECD's were in place and functioning at the designated crossings.
- St 12186+00 waterbar flow path requires maintenance and approximately MP 230.6 – 230.8 requires additional stabilization.

Recommend Corrective Action: Maintain all controls per the approved plan.

Deadline: Routine Maintenance 72 hours from notification

The recommended corrective action deadline date applies to all conditions noted on this report unless otherwise noted. If listed condition(s) currently constitute non-compliance and/or corrective actions are not completed by the deadline, other enforcement actions may be issued to the entity responsible for ensuring compliance on the above project.


Inspector Signature:  Date: 2-3-2020

FIELD INSPECTION PHOTO LOG

Project Name: Mountain Valley Pipeline

Date: Tuesday, January 14, 2020

- Fig. 1. Approximately MP 230.6 – 230.8 requires additional stabilization.

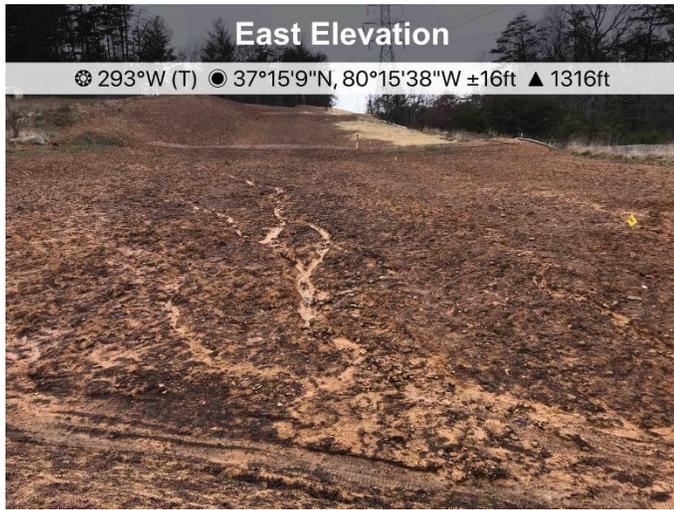

- Fig. 2. St 12186+00 waterbar flow path requires maintenance



- Fig. 3. Designated crossing S-C21, ECD's are in place and functioning.



- Fig. 4. St12116+00 permanent style waterbar has been installed and is functioning.

